
DOWNTOWN GREENWAY



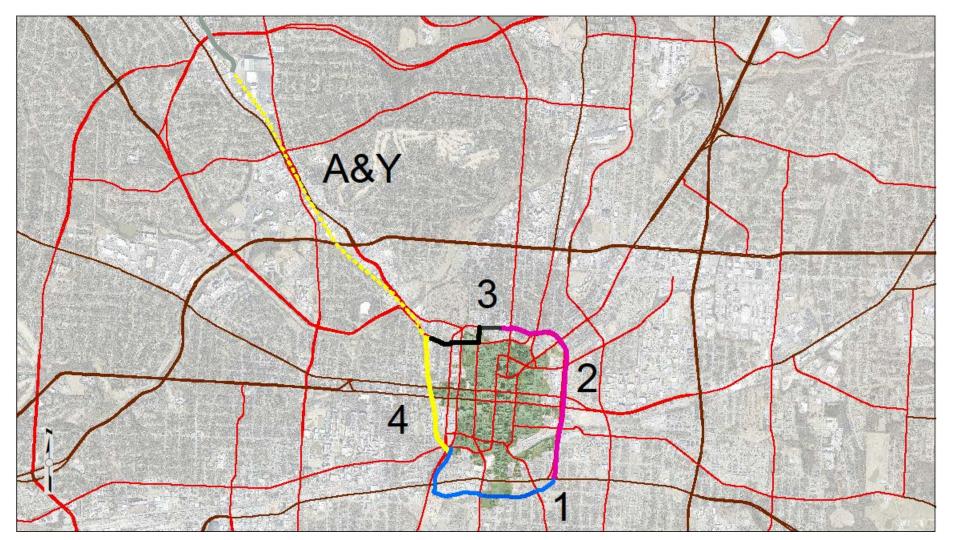

GREENWAY: MILESTONES

- 2001: Introduced in Center City Master Plan
- 2008: \$7M Street Improvement Bond Passed
- 2009: Construction Start
- 2010: First Section Opened: Five Points
- 2012: Morehead Park Section Opened
- 2013: Section at Smith Street Opened
- 2014: Tradition Cornerstone Opened

GREENWAY: TIMELINE/COST

	Construction Start / Complete	Total Cost
Phase 1 – South	Aug 2008 / Mar 2017	\$ 5,664,044
Phase 2 – East	Jan 2017 / May 2018	\$ 9,218,975
Phase 3 – North	Mar 2013 / May 2017	\$ 6,473,913
Phase 4 - West	2018-2019 *	\$ 8,927,054

CONSTRUCTION SCHEDULE


2016

- Southern, Eastern, and Northern sections start construction
- Build the Innovation Cornerstone
- Complete the functional design of Western section


2017-2018

- Complete engineering design and begin construction of Western section
- Build the Freedom Cornerstone

EXPENSES TO FEB 29, 2016

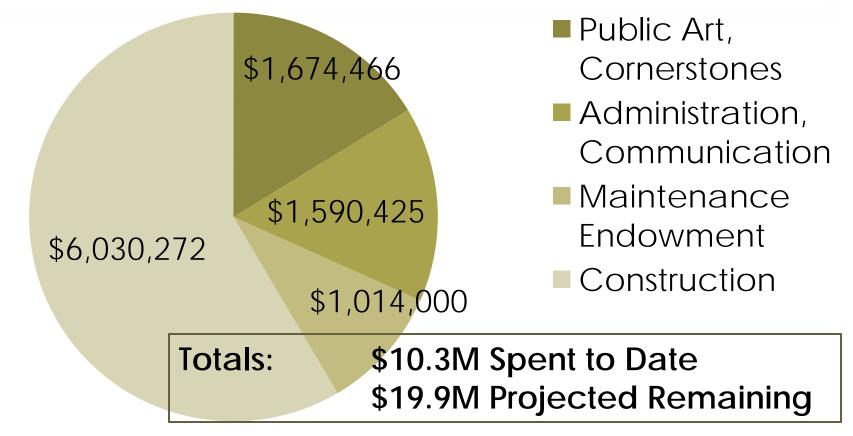

FUNDING: FEBRUARY 29, 2016

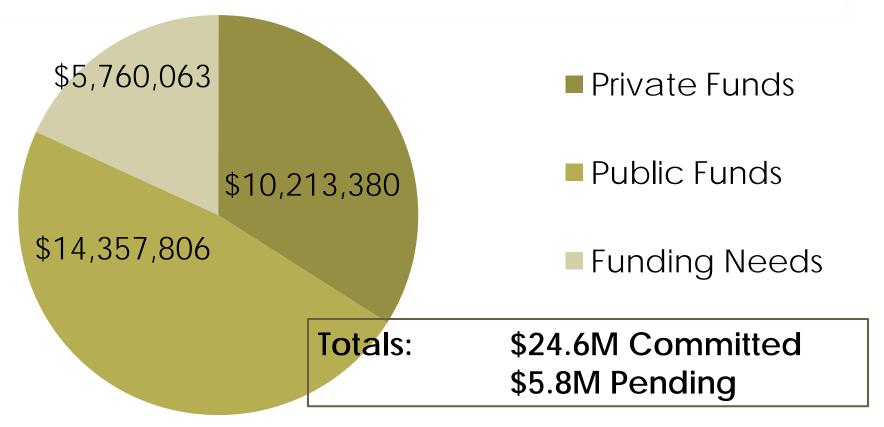



INVESTMENT

- Total: Completed \$57.5M
- Total Under Construction or Planned \$156.5M
- Total: \$214M

INVESTMENTS

South Elm Redevelopment Union Square Campus New Zion Church Fresh.Local.Good. Food Group Campus Crest Apartments Salvation Army Boys & Girls Club State Employees Credit Union Deep Roots Market Greenway at Fisher Park/Stadium View

Preyer Brewing/Crafted Street Food - AZ Properties Development Joymongers brewery Lindbrook Development Office Guilford and Prescott Streets – Dawn Chaney Arbor House Condominiums

> Total Complete Total Underway and Planned Total

\$80 million planned \$40 million underway \$6 million underway \$4 million planned \$25 million complete \$12 million underway \$3 million complete \$3 million complete \$10 million complete \$6 million complete \$1.5 million complete \$1 million underway \$13.5 million planned \$1 million complete \$8 million complete \$57.5 million \$156.5 million \$214 million

QUESTIONS?

