




4th Pool

Concept for 4th pool presented to City Council at special meeting on March 18, 2016

City Council voted (9-0) to support Resolution to approve \$20M of Hotel/Motel Tax Revenues to finance improvements to the Coliseum Complex on Apr. 5, 2016

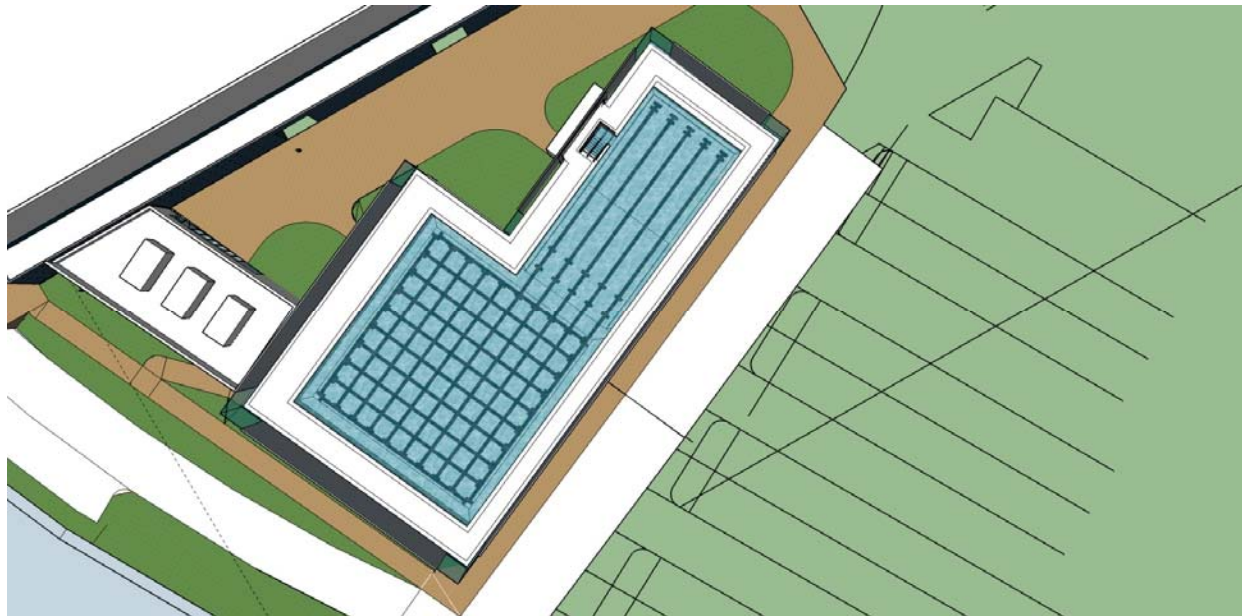


4th Pool


Total of 16-18 swimming lanes available (6-8 50 meter pool lanes; 10 lane 25-yard pool)


4th pool needed to accommodate growing demand of:


- *'Learn to Swim' Lessons*
- *Water Fitness/Water Aerobics classes*
- *High School & Club Swim Team Practices*
- *Recreational Lap Swimming*
- *Water Polo*
- *Synchronized Swimming*
- *Water Safety/Lifeguard Certification Classes*




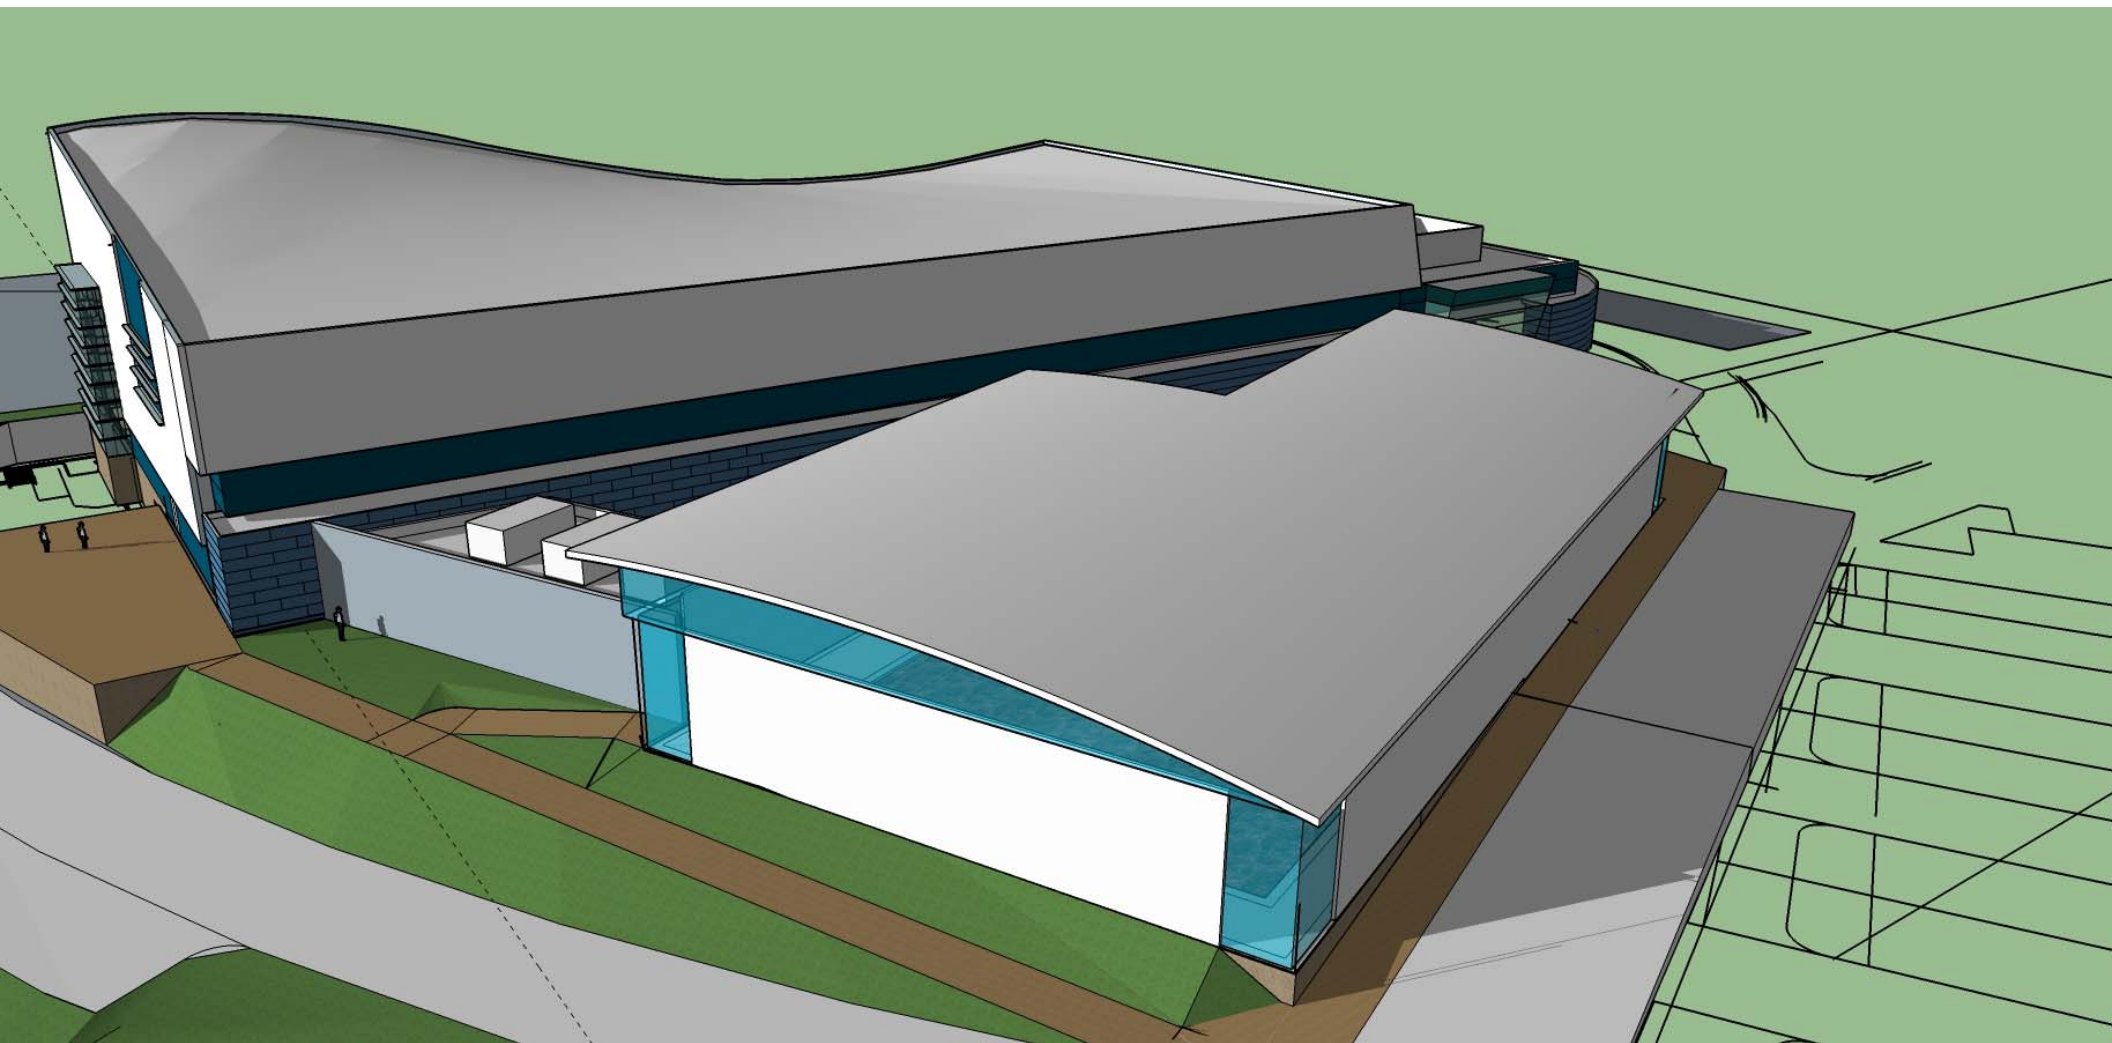


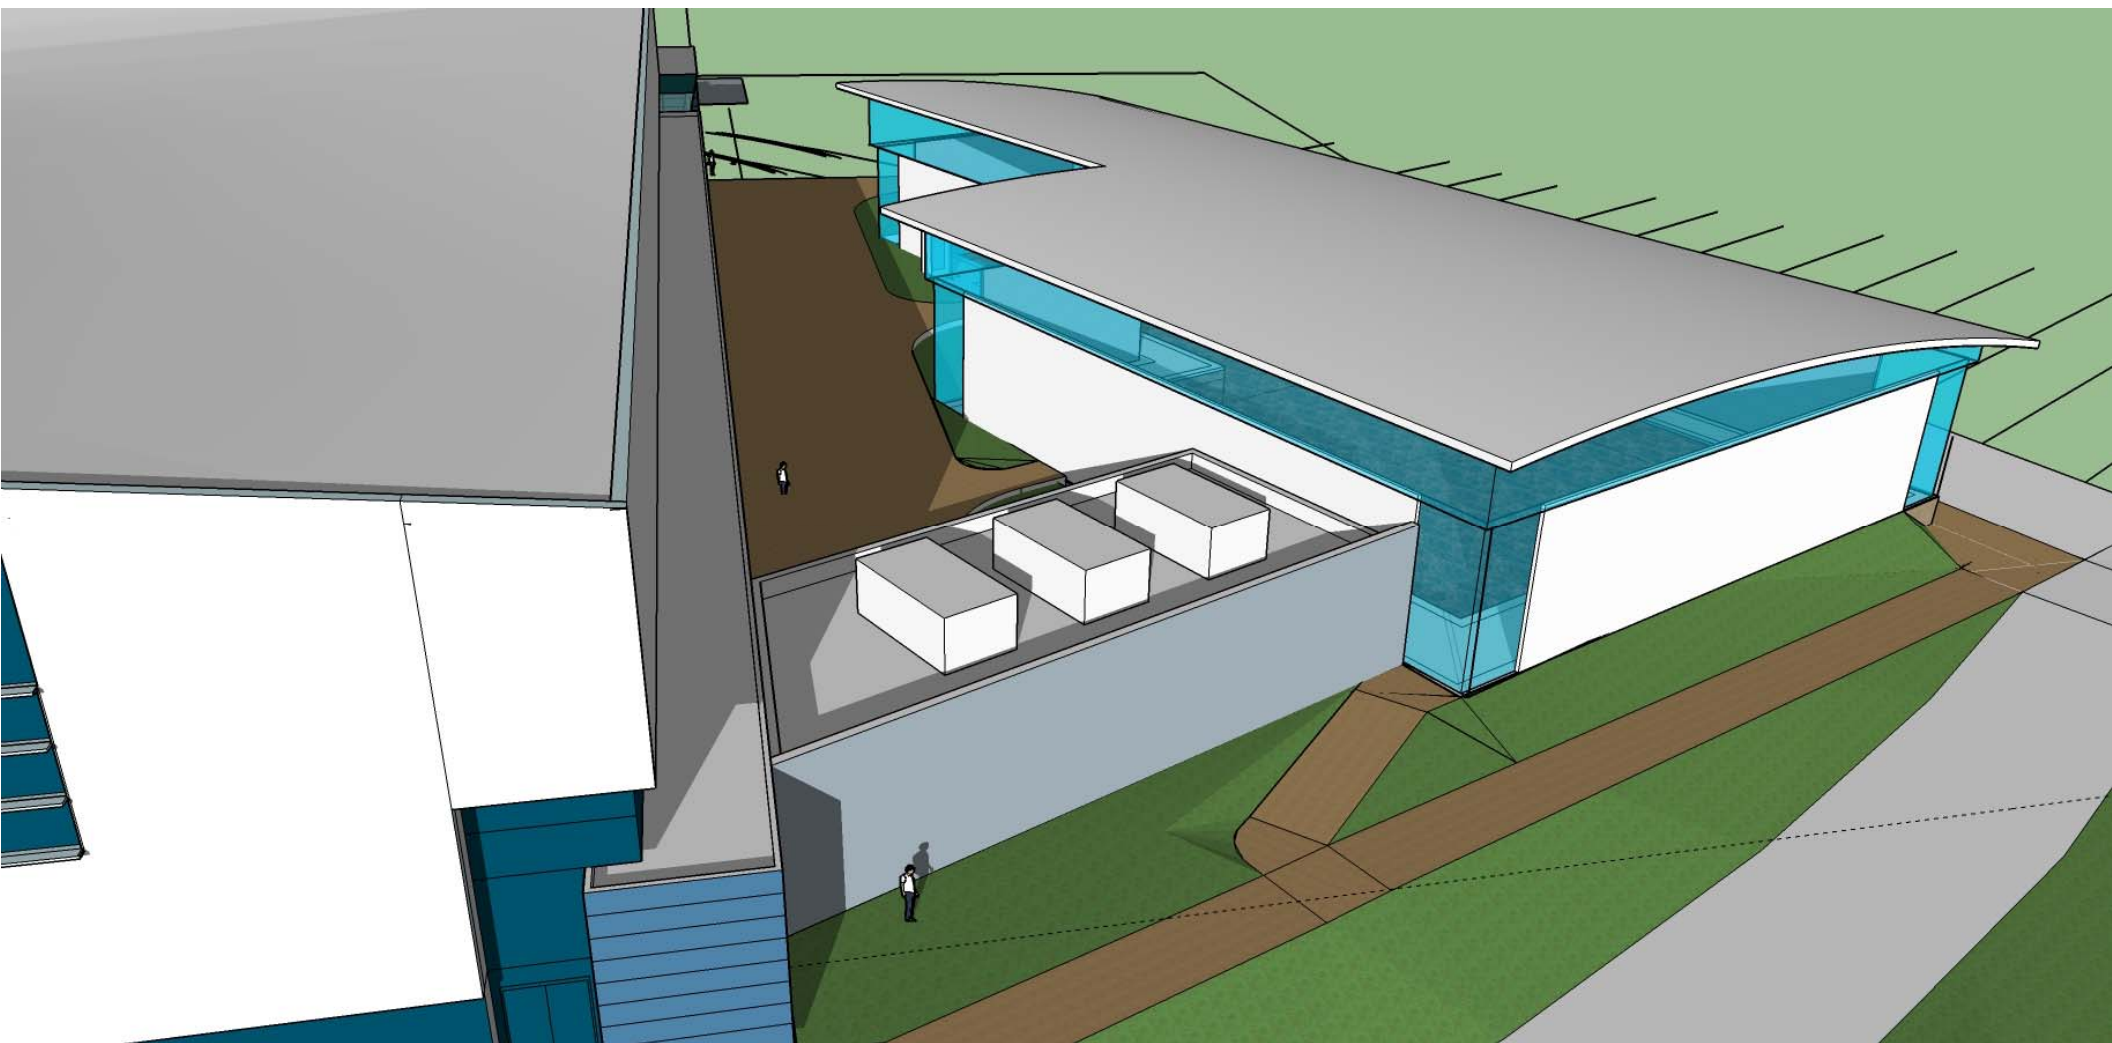


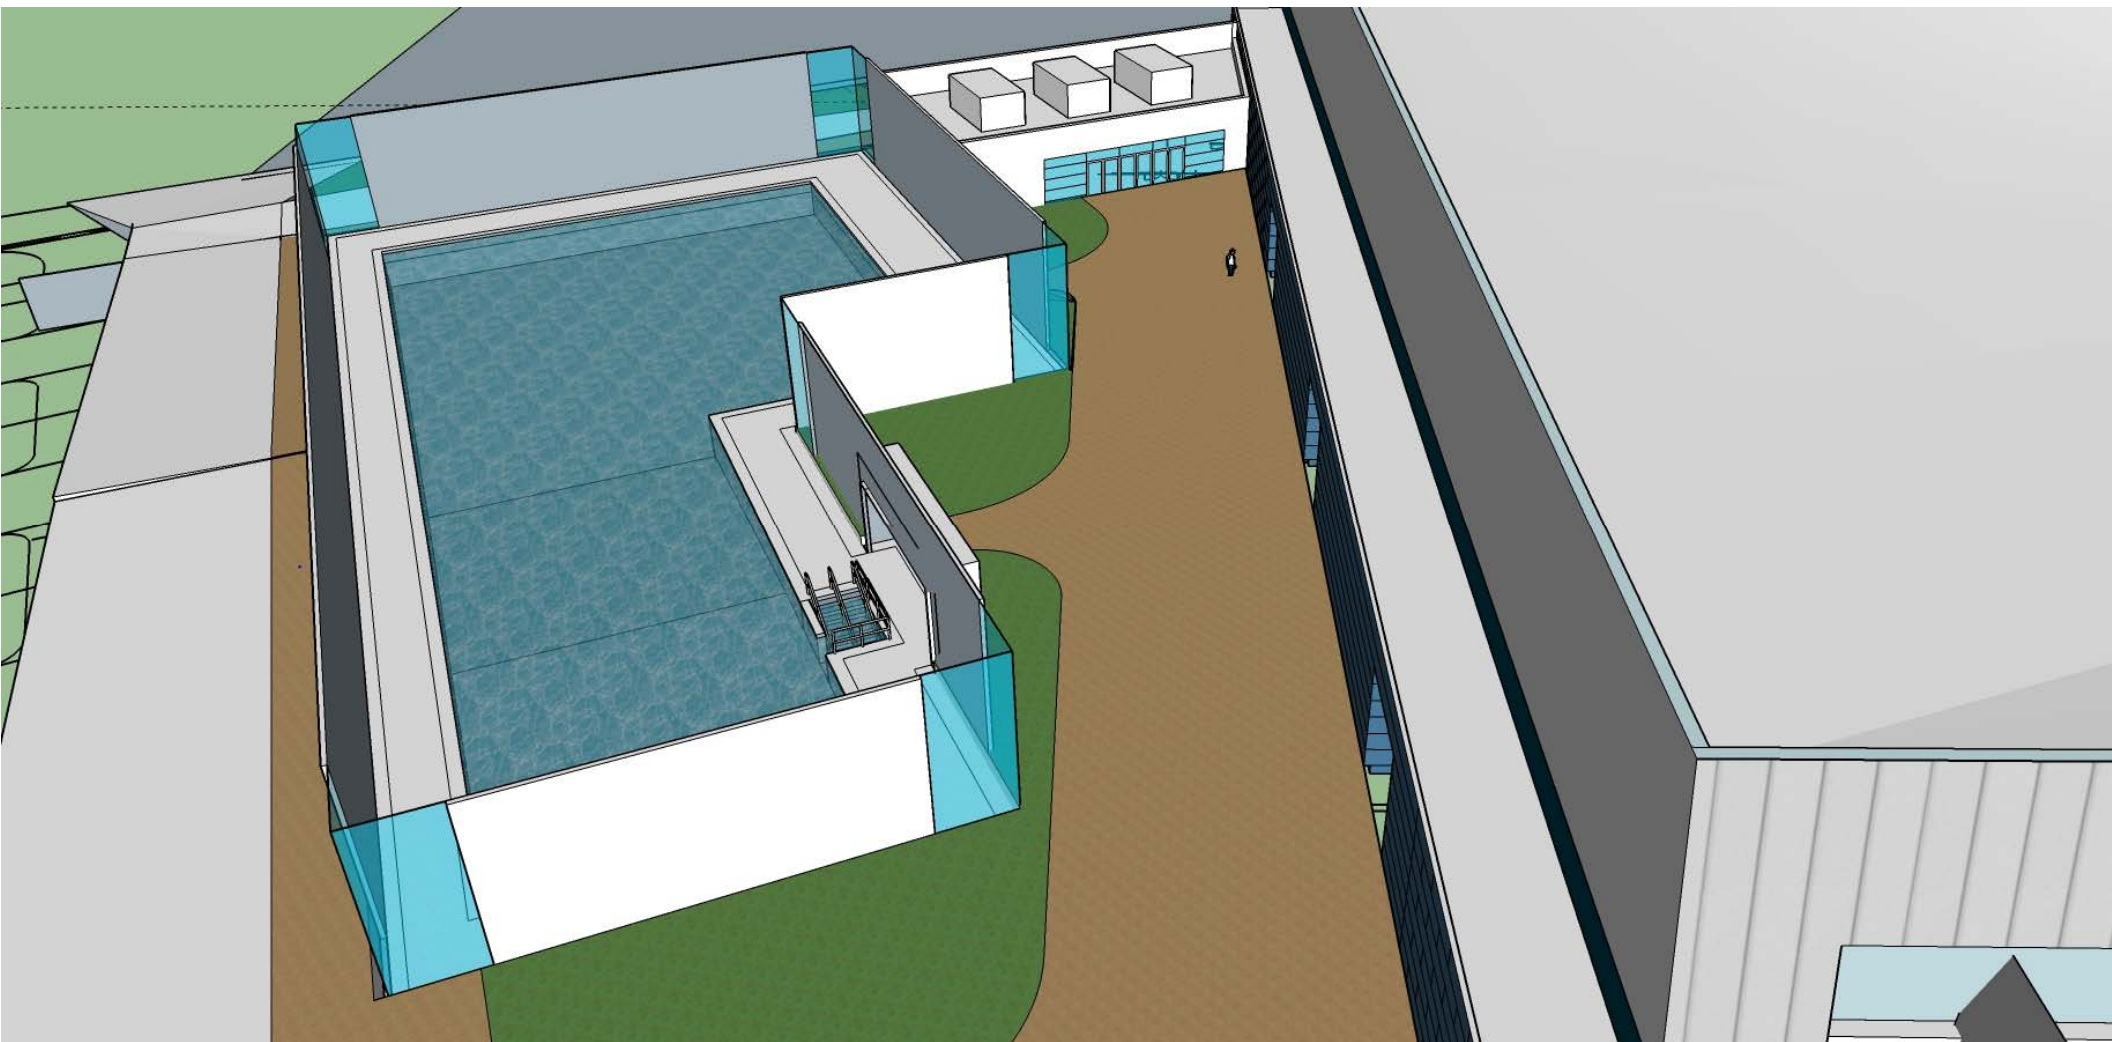

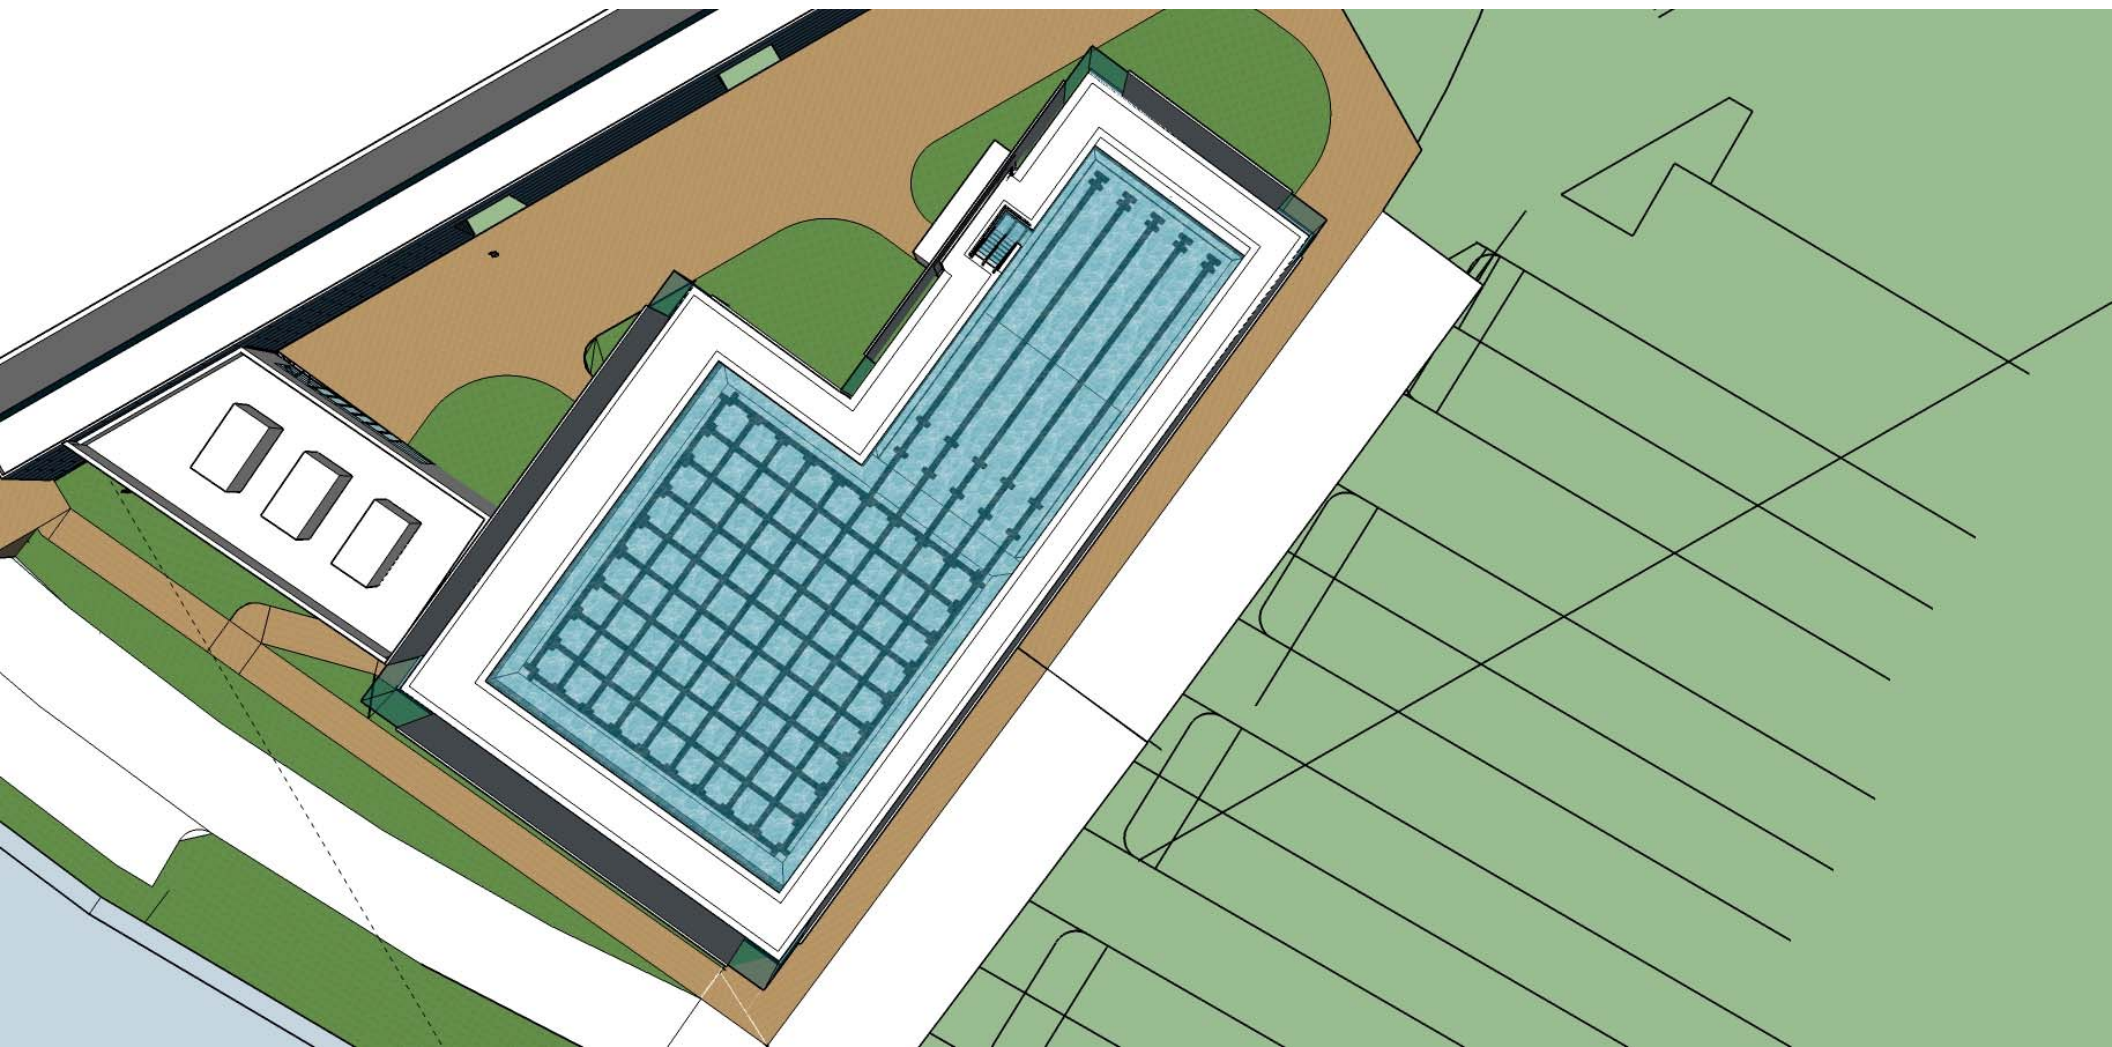

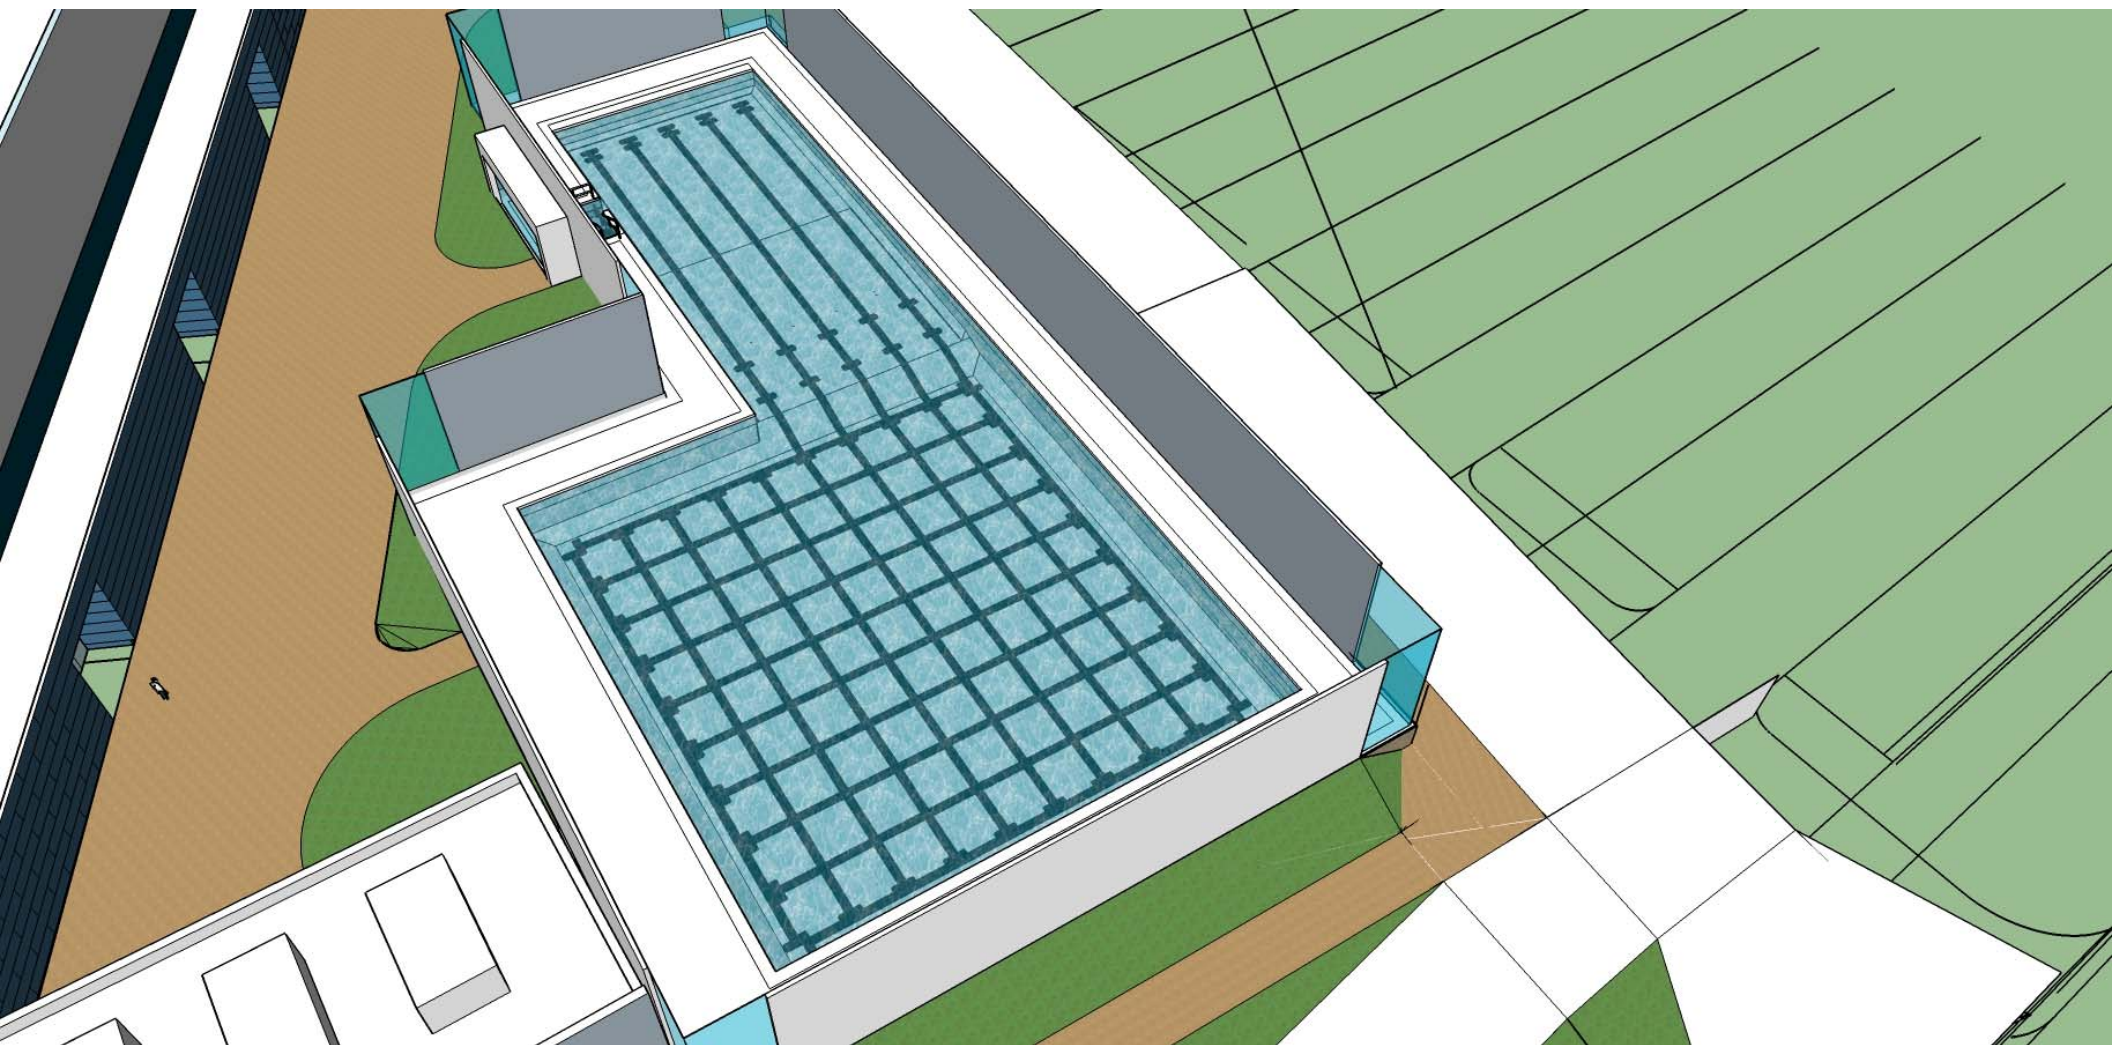

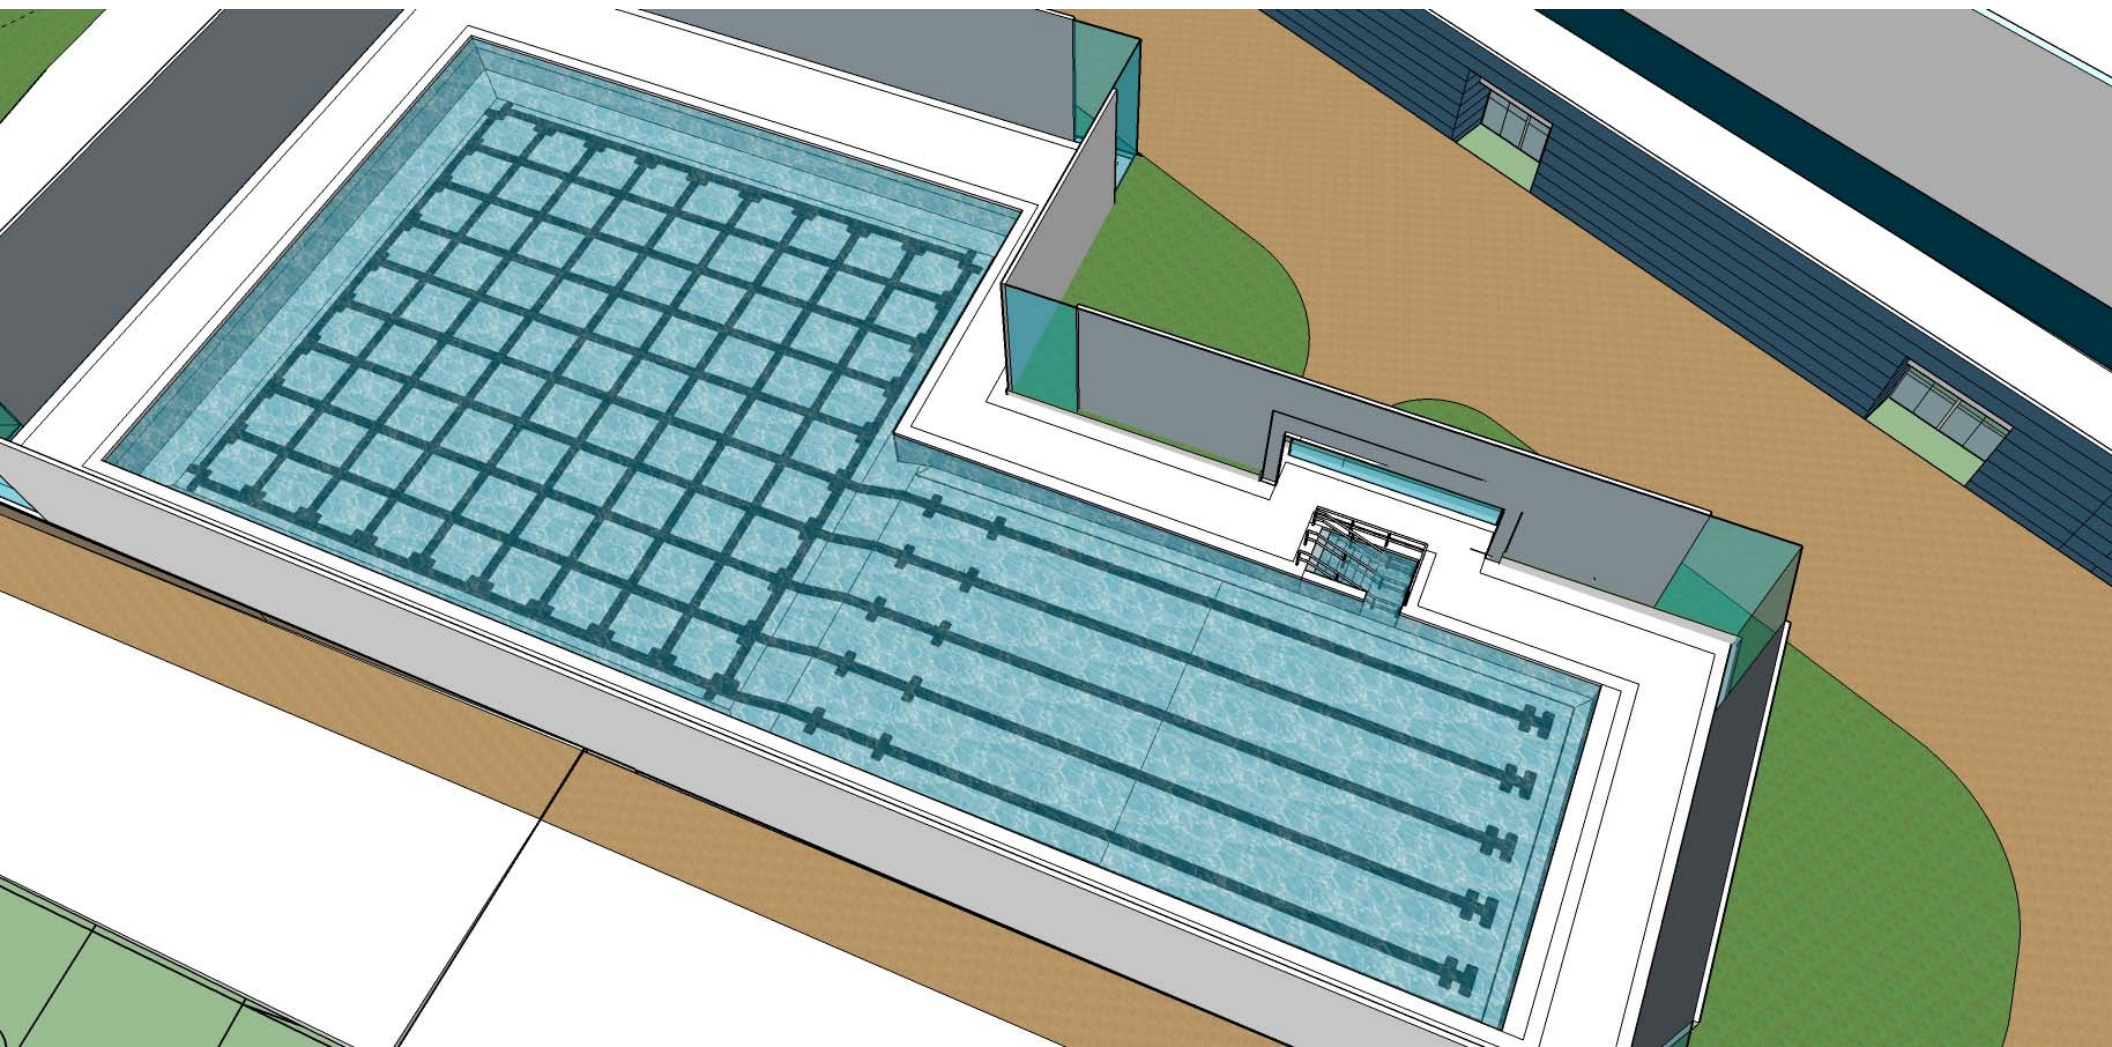

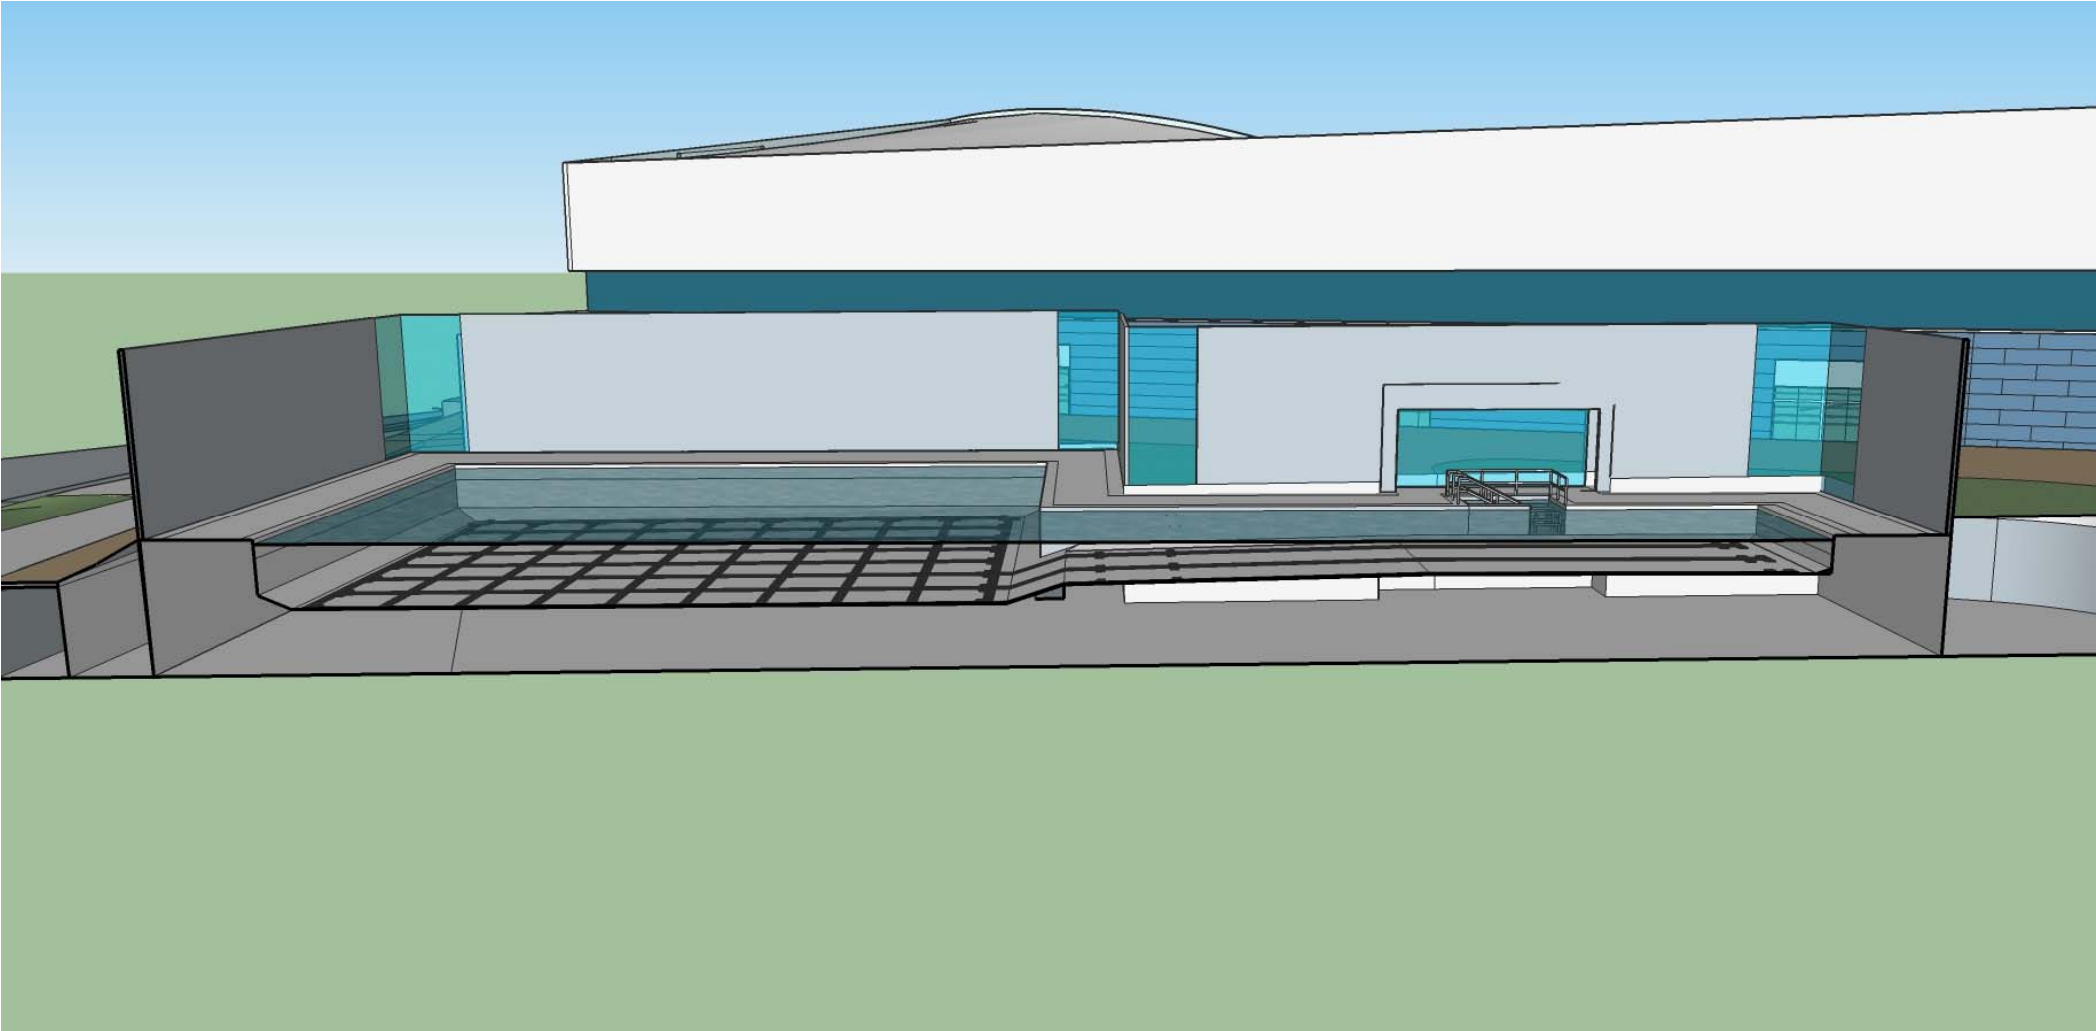



PHASE I

Site, grading and utility work

Construction began on 7/13/17

Contractor: D.H. Griffin Construction Company (Greensboro)

Cost: \$1.22M (\$1M less than Skanska-Retenbach initial bid)

Estimated Phase I completion date -- 10/31/17

PHASE II

Frank L. Blum Construction selected as Construction Manager Advisor to oversee General Contractor -- 6/28/17

Construction Drawings submitted to NCDOT and Greensboro Code Officials -- 7/7/17

RFQ/Prequalify General Contractors -- 8/14 – 8/31/17

Conduct MWBE Outreach with prequalified contractors -- date TBD

General Contractor Bids Issued -- 9/7/17*

General Contractor Bids Received -- 10/12/17*

General Contractor bid submitted for City Council approval -- 10/24/17*

**dates subject to NCDOT/City of GBO code review completion*
